

## CITY OF MINNEAPOLIS



Rick Kreuser

Project Manager

612-673-3624

[rick.kreuser@minneapolismn.gov](mailto:rick.kreuser@minneapolismn.gov)

# North Loop Paving Update

- Work completed this spring of 2020
  - Street Light installation, all luminaires installed
  - Tree planting and sod – complete
  - Punchlist work – complete
  - Sidewalk on 3<sup>rd</sup> St. next to Viridium (temp asphalt)
  - Seal Coat of Asphalt streets, schedule for July



















# C. J. Duffey PAPER COMPANY




# North Loop Sealcoating




Scheduled for mid July



# North Loop Pedestrian Improvements

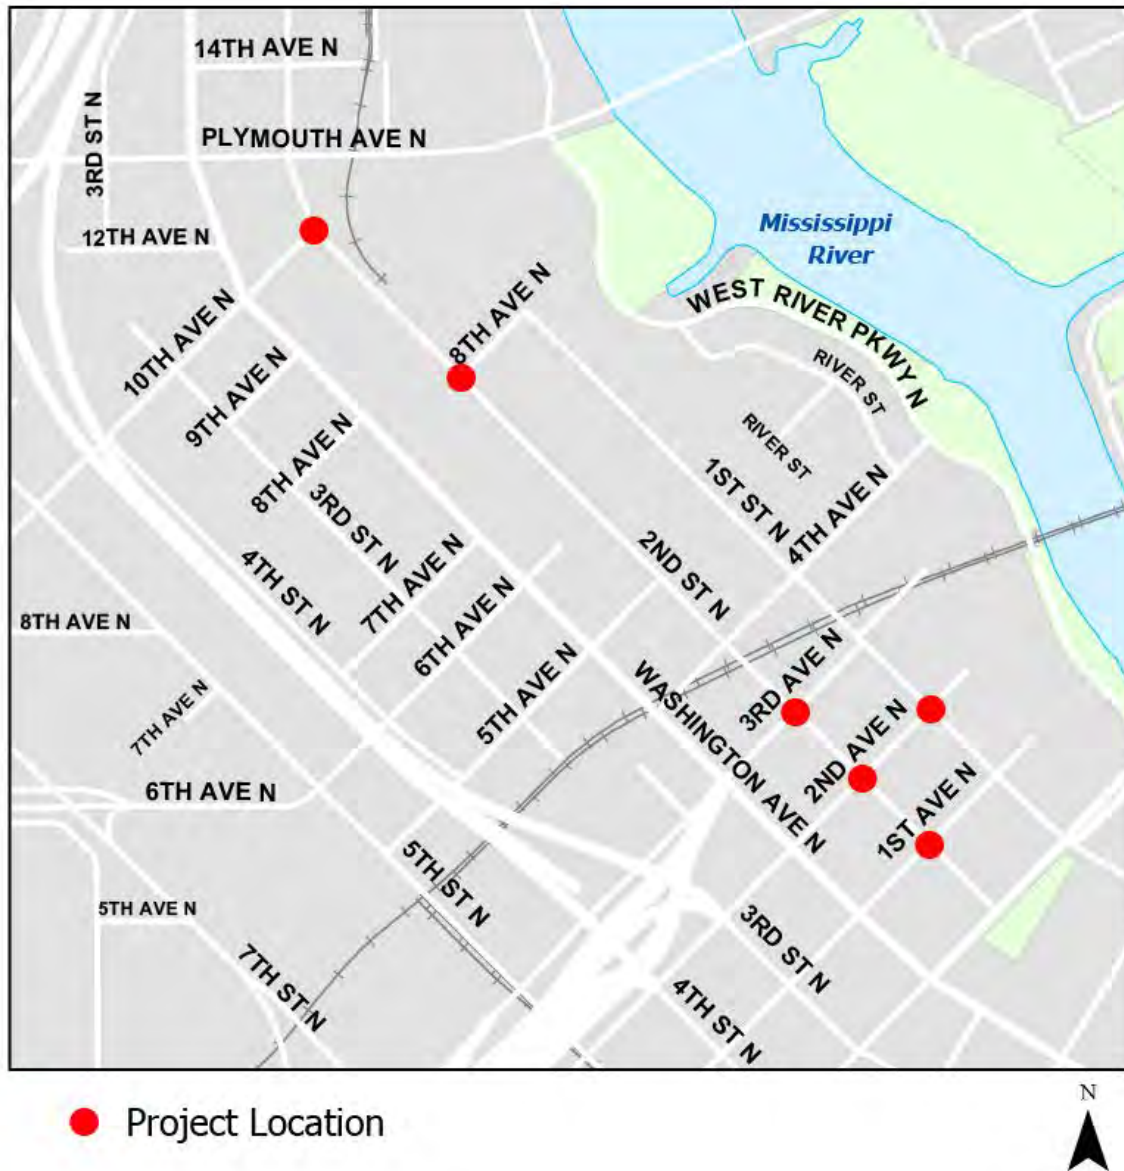

# North Loop Resurfacing

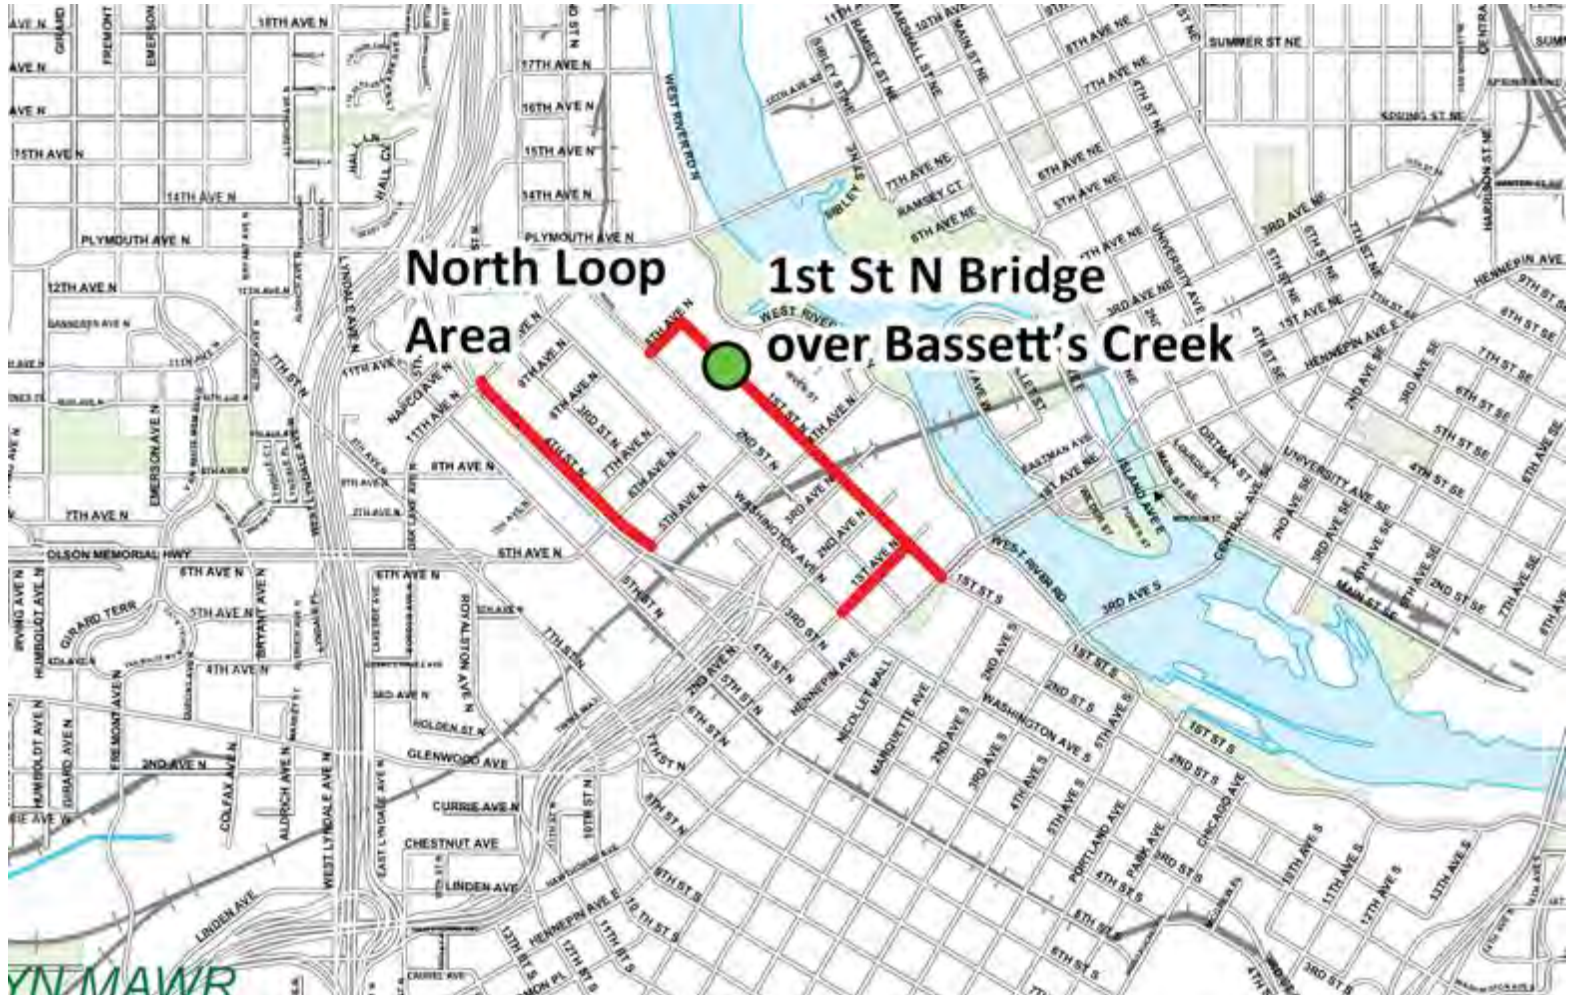

Schedule yet to be determined (Center Point work)



# CenterPoint Energy Gas Main Replacement

Anticipated Start Date = April 11

Two Phase Project

Phase 1 = RR to 8<sup>th</sup> Ave

Phase 2 = Hennepin to 2<sup>nd</sup> Ave

Work being done in advance of Mpls  
road improvement project

Engineering design incorporates modern  
materials and increased capacity

Ongoing project updates at  
[CenterPointEnergy.com/Construction](http://CenterPointEnergy.com/Construction)













































